


International Drive District


Transportation Progress Report


A large, semi-transparent blue graphic of an orange with several leaves is centered in the background. The orange is detailed with a grid of small dots, suggesting a mesh or a specific texture. The leaves are also semi-transparent and layered around the orange.



Challenges

- Supply Chain
- Term Contract
- Steel Costs
- Signal Cabinet and Supplies

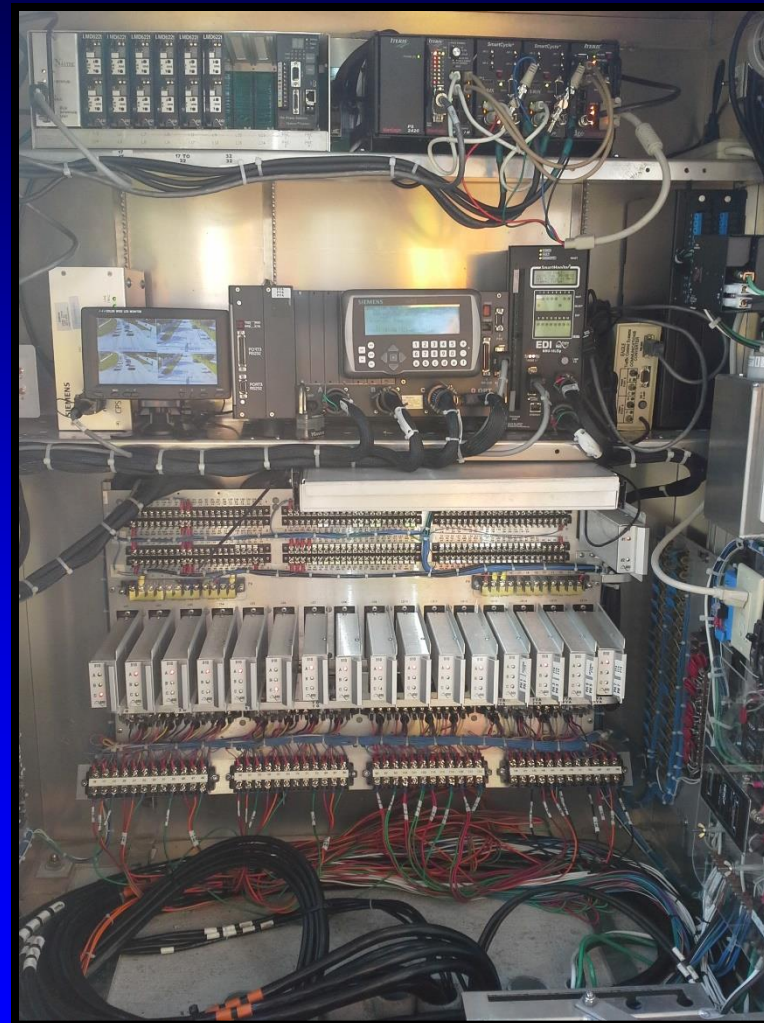




Project Updates

■ Project List

- Kirkman Road Extension
- Sand Lake Road (AVR to Turkey Lake Rd)
- I-Drive Transit Lanes
- Tradeshow Boulevard
- Pedestrian Safety Enhancements







Project Updates

■ Project List

- **Kirkman Road Extension**
- Sand Lake Road (AVR to Turkey Lake Rd)
- I-Drive Transit Lanes
- Tradeshow Boulevard
- Pedestrian Safety Enhancements

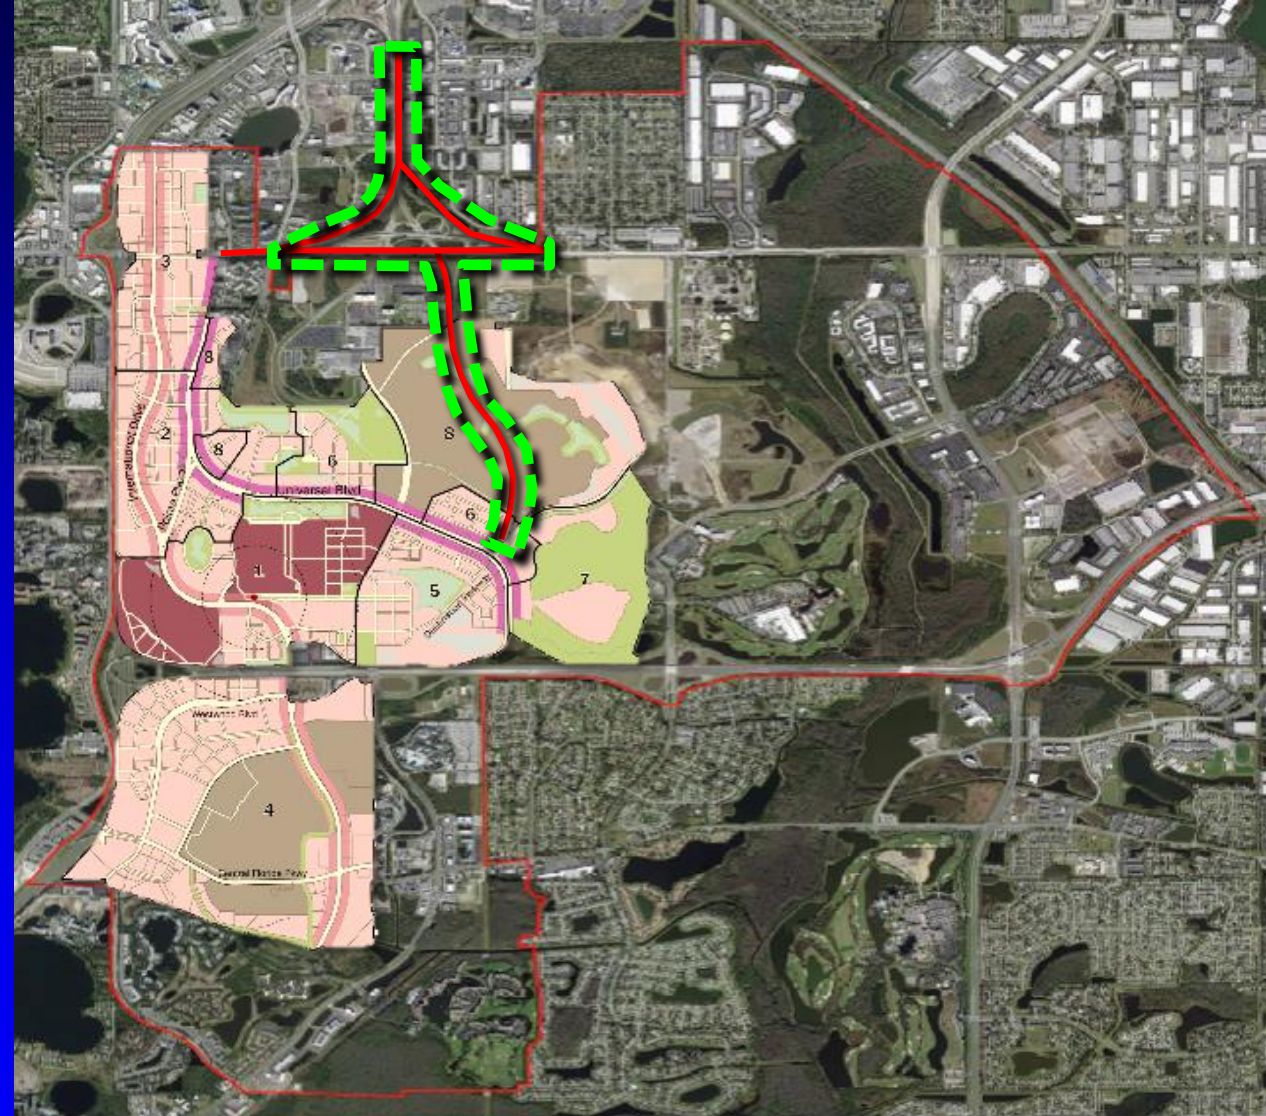




Project Updates

■ Kirkman Road Extension

- Universal Boulevard to Carrier Drive
- Construction started September 2021
- Utility work in progress
- Final Completion anticipated January 2025
- Orange County Jurisdiction
 - Segments 1 and 2: Universal Boulevard to Southern Interchange Ramps with Sand Lake Road
- FDOT Jurisdiction
 - Segment 3: Southern Interchange Ramps to Carrier Drive






Project Updates

- Kirkman Road Extension







Project Updates

■ Project List


- Kirkman Road Extension
- Sand Lake Road (AVR to Turkey Lake Rd)
- I-Drive Transit Lanes
- Tradeshow Boulevard
- Pedestrian Safety Enhancements

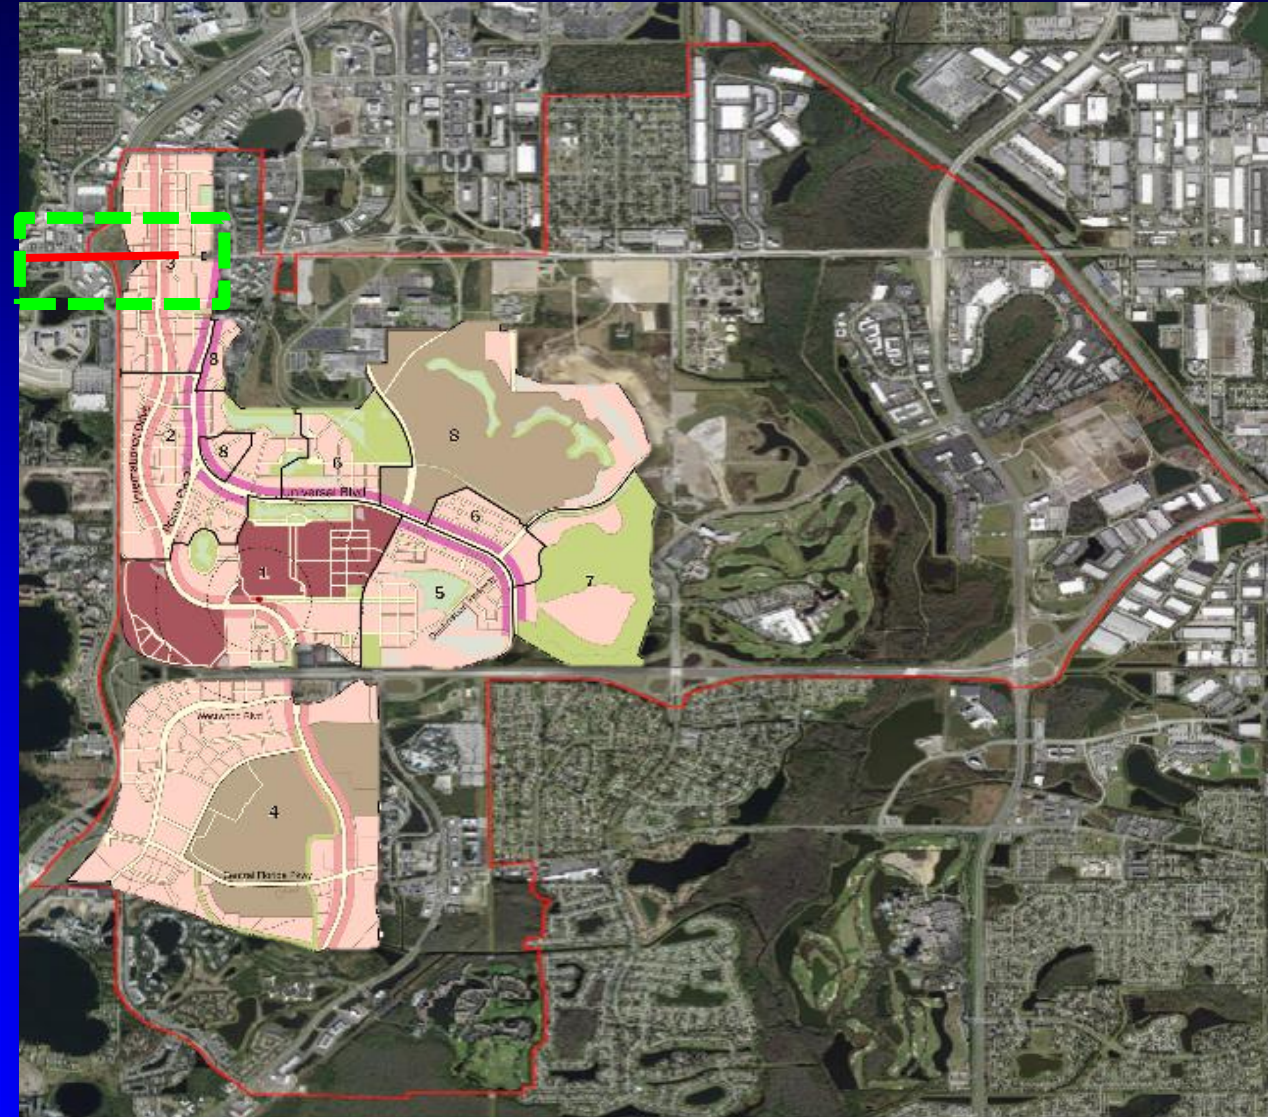




Project Updates

- **Sand Lake Road (AVR to Turkey Lake Road)**
 - Design is underway
 - Includes 10' wide shared use path on south side
 - Continuous EB and WB lanes for right turning vehicles between Rialto Dr. and Dr. Phillips Bv.
 - Traffic signal warrant study at the Fountain and Plaza Venezia
 - Construction expected to begin 2023

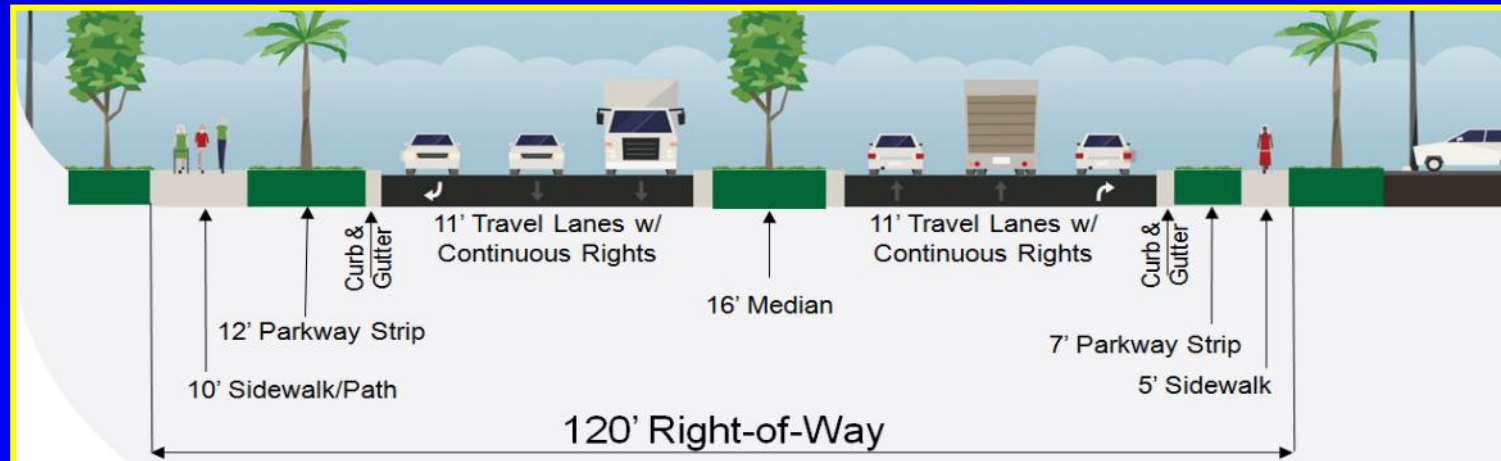





Project Updates

■ Project List

- Kirkman Road Extension
- Sand Lake Road (AVR to Turkey Lake Rd)
- **I-Drive Transit Lanes**
- Tradeshow Boulevard
- Pedestrian Safety Enhancements

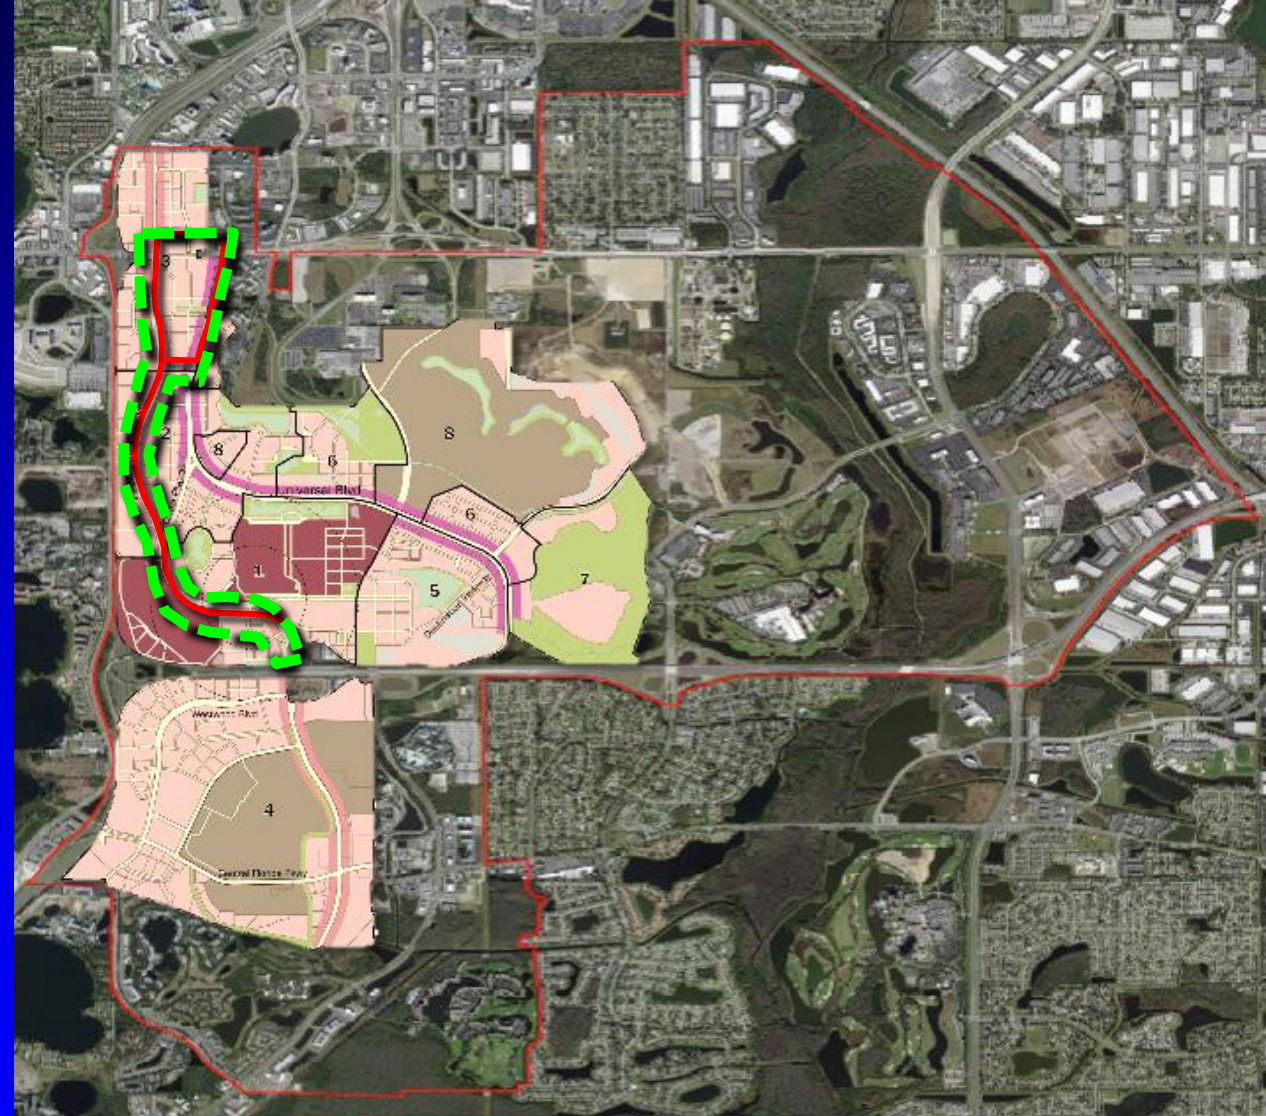





Project Updates

■ I-Drive Transit Lanes

- Destination Parkway to Sand Lake Road
- Utility Coordination, Survey & Plans Update
- Re-establishing Documents/Donations
- 24 Month Construction Project
 - Projected Start: Summer 2023
- Relieves Convention Center Congestion
- Accommodates I-Ride Trolley and Charter Buses
- Connector to Future Convention Center Circulator

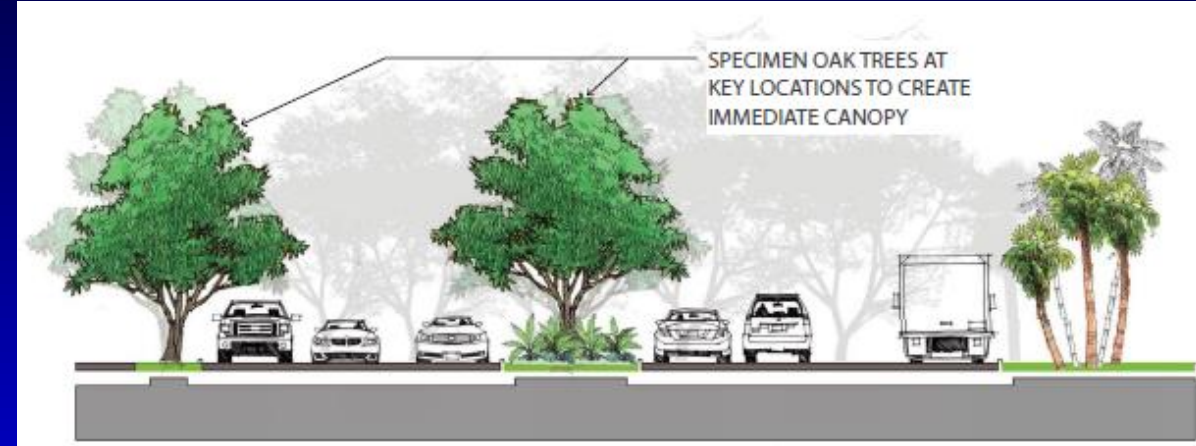





Project Updates

■ Project List

- Kirkman Road Extension
- Sand Lake Road (AVR to Turkey Lake Rd)
- I-Drive Transit Lanes
- **Tradeshow Boulevard**
- Pedestrian Safety Enhancements

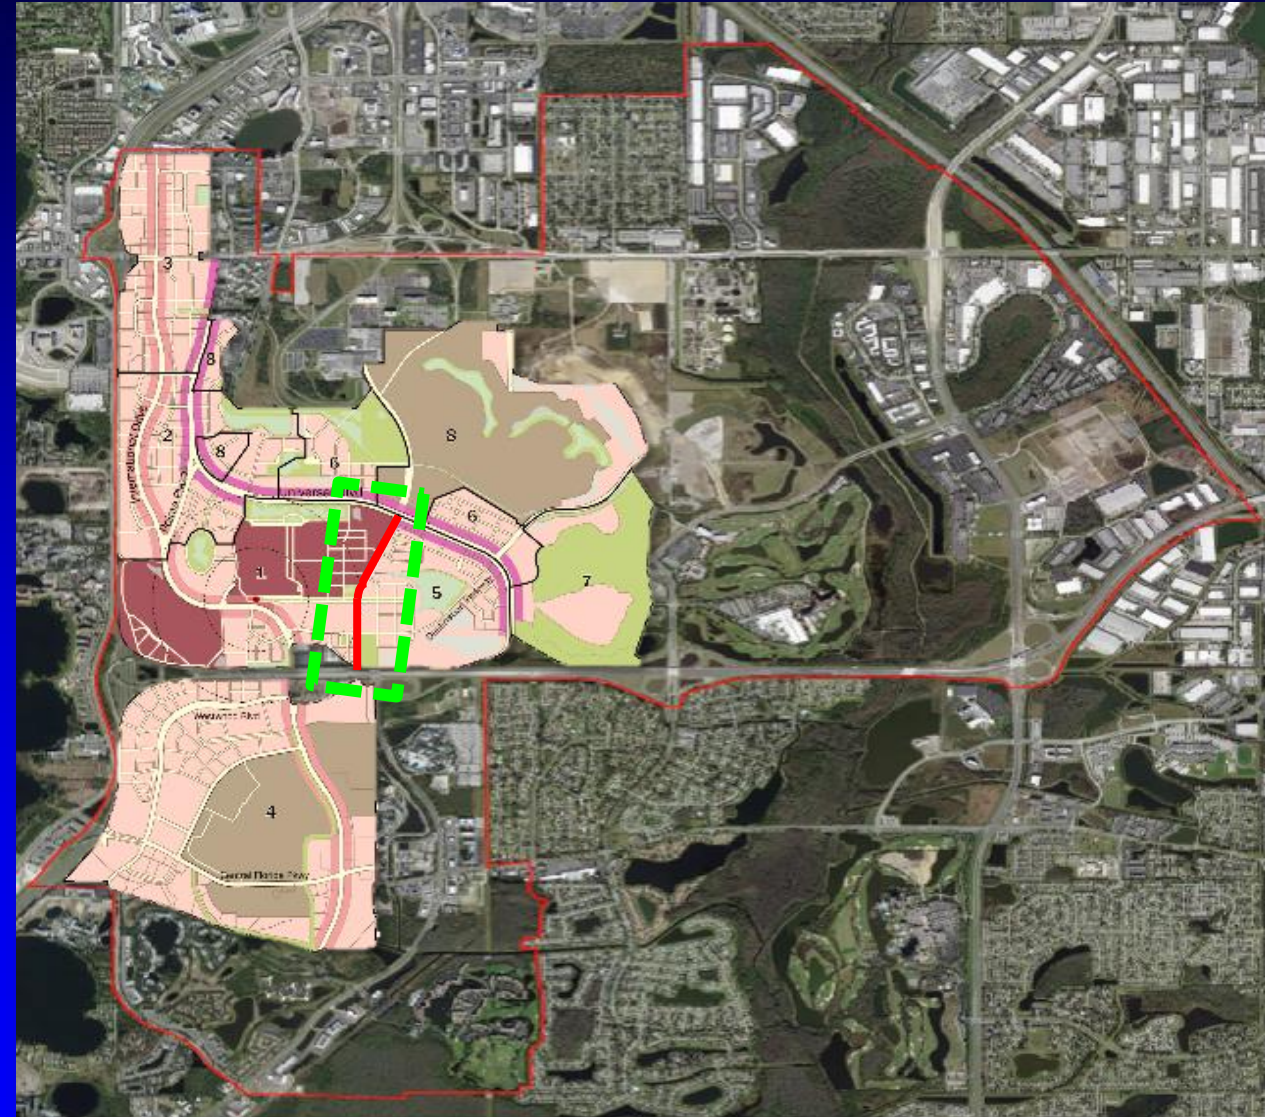





Project Updates

Tradeshow Boulevard

- Adds road, transit and freight capacity
- Supports convention center access for attendees and operational functions
- Connectivity with Kirkman Road Extension and Epic Universe
- BCC approved DRMP; working towards NTP

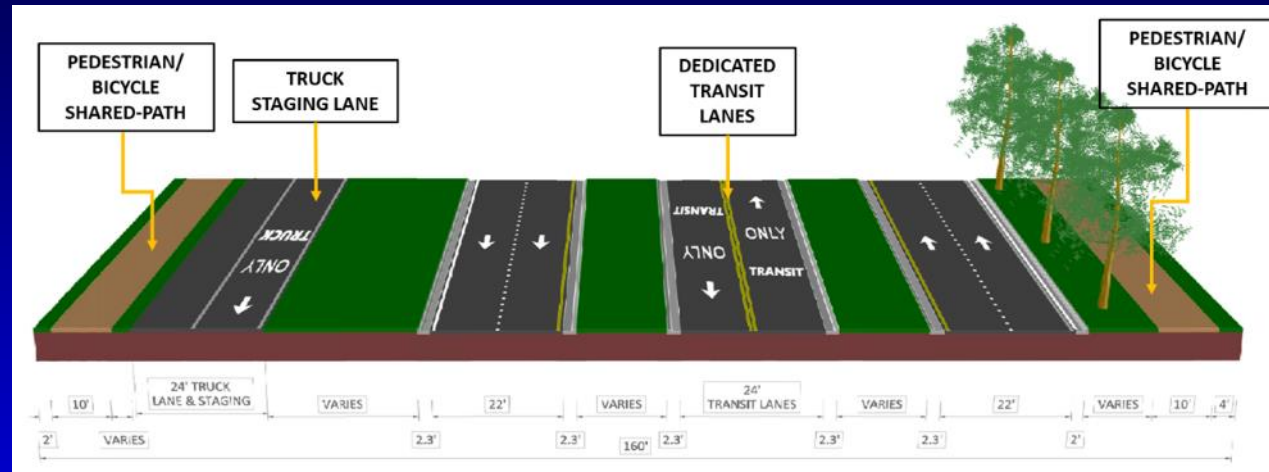




Project Updates

■ Project List

- Kirkman Road Extension
- Sand Lake Road (AVR to Turkey Lake Rd)
- I-Drive Transit Lanes
- Tradeshow Boulevard
- **Pedestrian Safety Enhancements**





Project Updates


Under Construction

- Hilton Las Palmeras/Universal Blvd
- Perimeter Road

Future Traffic Control

- Big Lake Cay Place
- Via Mercado
- Tradeshow Road/Kirkman Road extension
- Helicopter Rides/Ale House
- Austrian Court





Traffic Systems Projects

▪ Projects Underway

- Upgrade Traffic Adaptive
 - Pilot Project
 - International Drive Project
 - Signal Cabinet Replacement
 - Detection Replacement
- Upgrade of Communication Network
- Hyatt Mid-Block Crosswalk (FY 22/23)
- Challenges?

